

# WEEKLY CONSTRUCTION BULLETIN

(1/22/24 – 1/27/24)

**Brooklyn Dismantle Project PROJECT#: BBJ-KDSS BOROUGH: BROOKLYN DATE ISSUED: (1/19/24)**

The following is an anticipated work schedule for the upcoming week. However, due to unforeseen field and weather conditions, it may become necessary to change some scheduled work locations, operations, and dates.

DATE	WORK HOURS	LOCATION	OPERATION
1/22/24– 1/27/24	7:00 am– 5:00 pm	Brooklyn Detention Center (275 Atlantic Avenue)	<b>Weekly waste removal and refuse container pick-up and drop-off</b> (Noise / Work will take place inside perimeter fencing with no public interaction)
1/22/24– 1/26/24	7:00 am– (M – Fri) 10:00 pm <b>*SEE BELOW</b>	Brooklyn Detention Center (275 Atlantic Avenue) <b>*Work to end at 9:30 pm &amp; site shutdown at 10:00 pm*</b>	<b>Interior/exterior tower structural dismantling (4th &amp; 5th Floor interior demo / 7th floor wall and slab removal)</b> (Noise/Vibrations)
1/22/24– 1/26/24	7:00 am– (M – Fri) 10:00 pm <b>*SEE BELOW</b>	Brooklyn Detention Center (275 Atlantic Avenue) <b>*Work to end at 9:30 pm &amp; site shutdown at 10:00 pm*</b>	<b>7th floor scaffold removal (M-F) / Courtyard Wall Demo (M&amp;T)</b> (Noise)
1/27/24	9:00 am– 5:00 pm	Brooklyn Detention Center (275 Atlantic Avenue)	<b>Interior/exterior tower structural dismantling (4th floor interior demo / 7th floor wall and slab removal / Waste removal)</b> (Noise/Vibrations)

**\*Department of Buildings (DOB) approved After Hours Variance (AHV)**

**\*M-Fri: Shift 1 (7:00 am - 5:00 pm)  
Shift 2 (3:00 am - 10:00 pm)  
\*Sat: 9:00 am – 5:00 pm**

**WATER SHUT-OFF NOTIFICATIONS:** In addition to a 72-hour Advisory, prior 24-hour notification will be distributed/posted to any / all affected locations(s).

**NO PARKING SIGNS:** Will be distributed/posted 72 hours prior to the temporary elimination of street parking. Please observe posted parking regulations in construction areas.

**FOR FURTHER INFORMATION:** Contact **Lucien Allen**, the **Community Construction Liaison** at (917) 270 - 2370 or **BrooklynCCL@bbjnyc.com**

# Overview of Dismantle Activities & Progress

Interim sally port & officer booth

Oil Tank Removal

Internal & External Structural Dismantling


Podium dismantle progress

Tower netting

Tower scaffolding

MTA Vent Shafts

275 Atlantic Ave.

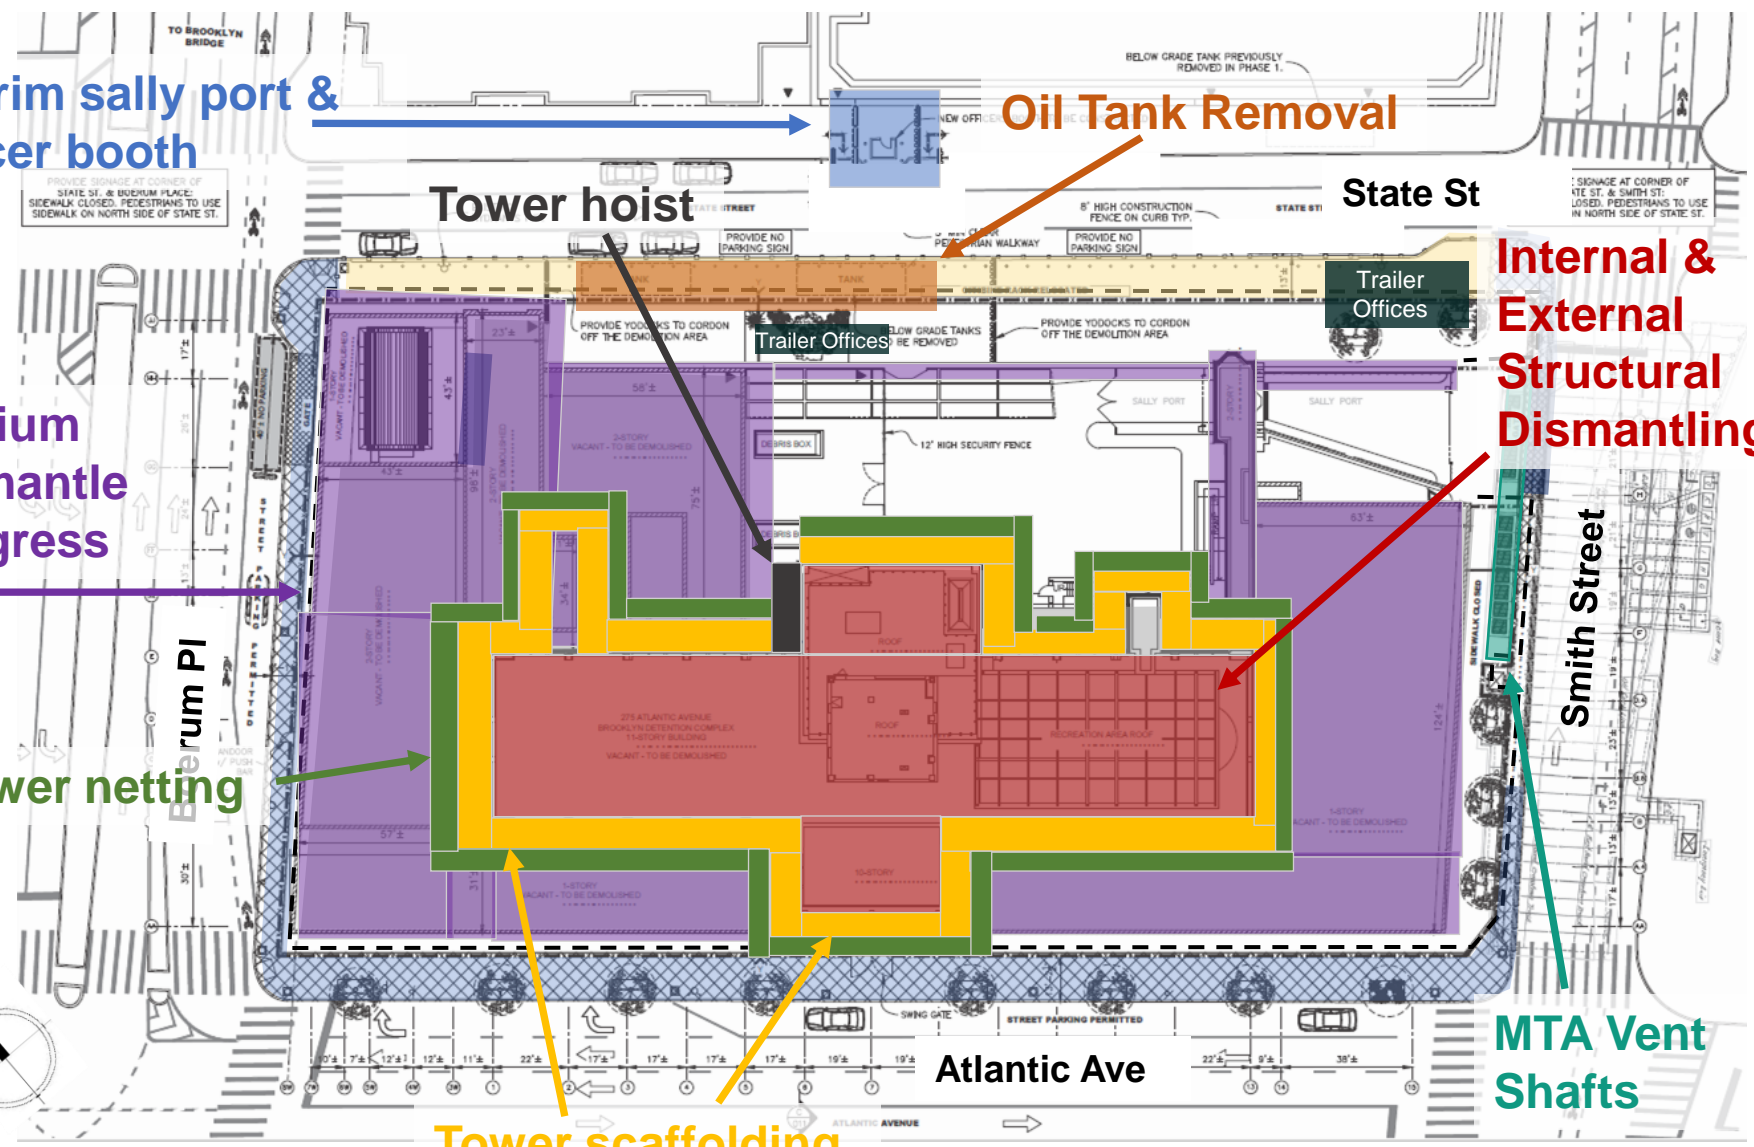

	8' HIGH SIDEWALK SHED
	16' HIGH SIDEWALK SHED
	CONSTRUCTION PLYWOOD FENCE
	SECURITY FENCE
	8' HIGH CONSTRUCTION FENCE ON CURB TYP.
	TA GRATING OVER VENTILATION STRUCTURE
	FIRE DEPARTMENT CONNECTION FOR SPRINKLER & STANDPIPE TO REMAIN
	DIRECTION OF TRAFFIC
	TREE WITH PROTECTION
	FIRE HYDRANT
	STREET SIGN
	YODOCKS TYP
	Sidewalk Closure
	Oil tank removal
