

WEEKLY CONSTRUCTION BULLETIN

(2/12/24 – 2/17/24)

Brooklyn Dismantle Project PROJECT#: BBJ-KDSS BOROUGH: BROOKLYN DATE ISSUED: (2/9/24)

The following is an anticipated work schedule for the upcoming week. However, due to unforeseen field and weather conditions, it may become necessary to change some scheduled work locations, operations, and dates.

| DATE(S) | WORK HOURS | LOCATION | OPERATION |
|-----------------------|--|--|---|
| 2/12/24– 2/17/2024 | 7:00 am–10:00 pm | Brooklyn Detention Center (275 Atlantic Avenue) | Weekly waste removal and refuse container pick-up and drop-off (Intermittent noise and vibrations due to container loading) |
| 2/12/24– 2/17/2024 | 7:00 am–10:00 pm (M – Fri) *Work to end at 9:30 pm & site shutdown at 10:00 pm* | Brooklyn Detention Center (275 Atlantic Avenue) | Scaffold removal (Noise / Vibrations) |
| 2/12/24– 2/13/2024 | 7:00 am–10:00 pm (M – Fri) | Brooklyn Detention Center (275 Atlantic Avenue) | Sheet Pile Installation (Shoring - State St. Tank Excavation) (Noise / Continuous Vibrations; Loud noises and stronger vibrations may be experienced when sheet piles hit subsurface impediments) |
| 2/14/24– 2/15/2024 | 7:00 am–10:00 pm (M – Fri) | Brooklyn Detention Center (275 Atlantic Avenue) | Tank Removal (State St. Tank Excavation) (Noise / Vibrations; Tank removal by long-reach excavators) |
| 2/16/24– 2/17/2024 | 7:00 am–10:00 pm (M – Fri) | Brooklyn Detention Center (275 Atlantic Avenue) | Backfill (State St. Tank Excavation) (Noise / Vibrations) |
| 2/17/2024 | 9:00 am–5:00 pm *M-Fri: Shift 1 (7:00 am - 5:00 pm) Shift 2 (3:00 am – 10:00 pm) *Sat: 9:00 am – 5:00 pm | Brooklyn Detention Center (275 Atlantic Avenue) | Waste Removal / Backfill / Tank Removal / Scaffold Removal / Hoist Removal (Noise / Vibrations; *See detailed descriptions above) |

WATER SHUT-OFF NOTIFICATIONS: IN ADDITION TO A 72-HOUR ADVISORY, PRIOR 24-HOUR NOTIFICATION WILL BE DISTRIBUTED/POSTED TO ANY / ALL AFFECTED LOCATIONS(S).


NO PARKING SIGNS: WILL BE DISTRIBUTED/POSTED 72 HOURS PRIOR TO THE TEMPORARY ELIMINATION OF STREET PARKING. PLEASE OBSERVE POSTED PARKING REGULATIONS IN CONSTRUCTION AREAS.

For further information: Contact **Lucien Allen**, the **Community Construction Liaison** at (917) 270 - 2370 or **BrooklynCCL@bbjnyc.com**

Eric Adams,
Mayor

Thomas Foley, P.E.
Commissioner

Overview of Dismantle Activities & Progress

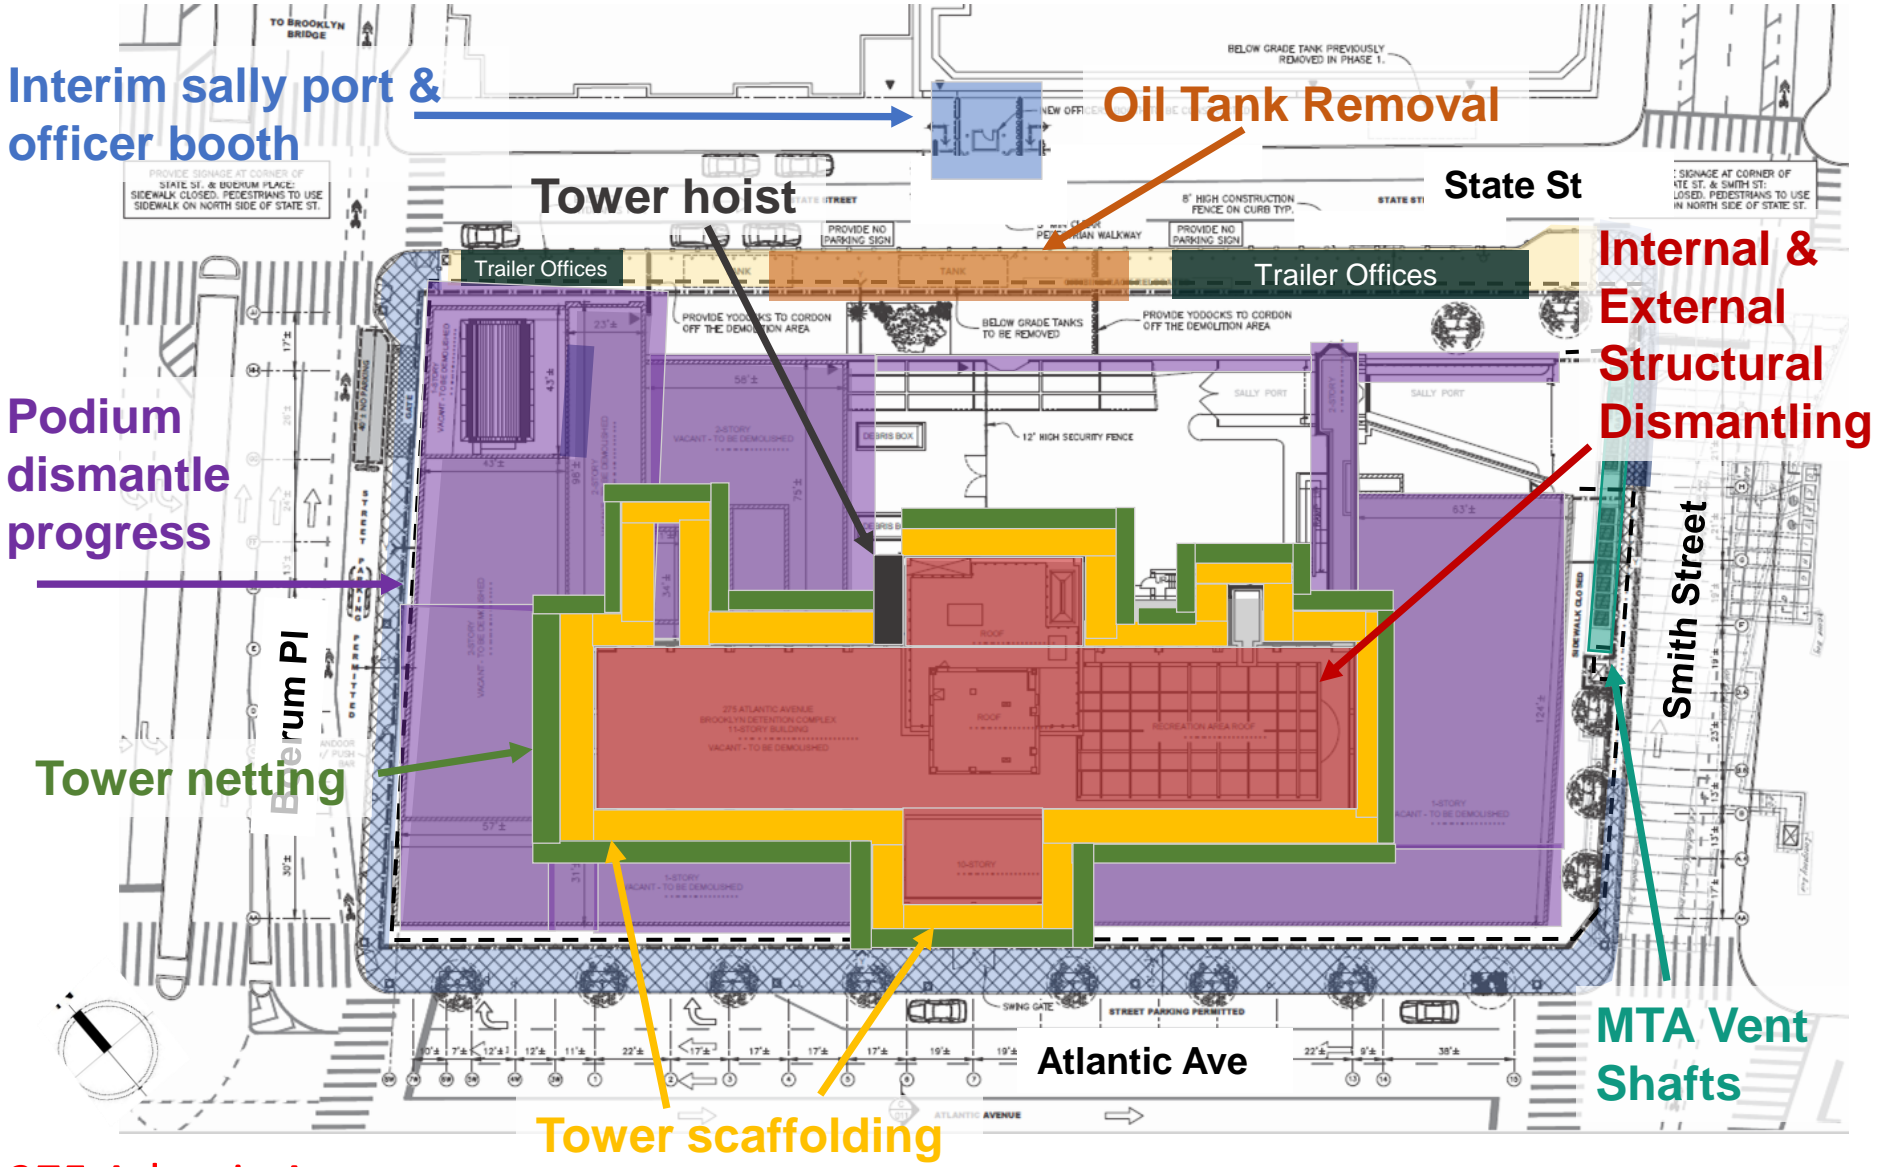

| | |
|--|--|
| | 8' HIGH SIDEWALK SHED |
| | 16' HIGH SIDEWALK SHED |
| | CONSTRUCTION PLYWOOD FENCE |
| | SECURITY FENCE |
| | 8' HIGH CONSTRUCTION FENCE ON CURB TYP. |
| | TA GRATING OVER VENTILATION STRUCTURE |
| | FIRE DEPARTMENT CONNECTION FOR SPRINKLER & STANDPIPE TO REMAIN |
| | DIRECTION OF TRAFFIC |
| | TREE WITH PROTECTION |
| | FIRE HYDRANT |
| | STREET SIGN |
| | YODOCKS TYP |
| | Sidewalk Closure |
| | Oil tank removal |

275 Atlantic Ave.
