

WEEKLY CONSTRUCTION BULLETIN

(3/25/24 – 3/30/24)

Brooklyn Dismantle Project PROJECT#: BBJ-KDSS BOROUGH: BROOKLYN DATE ISSUED: (3/22/24)

The following is an anticipated work schedule for the upcoming week. However, due to unforeseen field and weather conditions, it may become necessary to change some scheduled work locations, operations, and dates.

DATE(S)	WORK HOURS	LOCATION	OPERATION
3/25/24 – 3/30/24	7:00 am–9:00 pm (M - F) 9:00 am – 5:00 pm (Sat)	Brooklyn Detention Center (275 Atlantic Avenue)	Weekly waste removal and refuse container pick-up and drop-off (Intermittent noise and vibrations due to container loading)
3/26/24 – 3/30/24	7:00 am–9:00 pm (M - F) 9:00 am – 5:00 pm (Sat)	Brooklyn Detention Center (275 Atlantic Avenue)	North Yard Dismantling (Noise / Vibrations / Dismantling will commence by breaking the concrete deck with a demo hammer mounted to a track excavator / Noise will be like previous tower dismantle hammering activities)
3/25/24 – 3/30/24	7:00 am–9:00 pm (M - F) 9:00 am – 5:00 pm (Sat)	Brooklyn Detention Center (275 Atlantic Avenue)	Install Berm (Noise / Gravel will be trucked into the site and spread around the interior of the foundation using front-end loaders to prevent perimeter soil from shifting inward)
3/28/24 – 3/30/24	7:00 am–9:00 pm (M - F) 9:00 am – 5:00 pm (Sat)	Brooklyn Detention Center (275 Atlantic Avenue)	Remove Perimeter Wall (Noise / Remaining podium wall will be removed using a demo hammer, mounted to a track excavator / Noise will be like previous tower dismantle hammering activities / Water will be used for dust suppression)
Extended Work Hours: Mon – Fri: (7:00 am – 9:00 pm) Sat: (9:00 am – 5:00 pm)			*Site will shut down at 9:00 pm

WATER SHUT-OFF NOTIFICATIONS: IN ADDITION TO A 72-HOUR ADVISORY, PRIOR 24-HOUR NOTIFICATION WILL BE DISTRIBUTED/POSTED TO ANY / ALL AFFECTED LOCATIONS(S).

NO PARKING SIGNS: WILL BE DISTRIBUTED/POSTED 72 HOURS PRIOR TO THE TEMPORARY ELIMINATION OF STREET PARKING. PLEASE OBSERVE POSTED PARKING REGULATIONS IN CONSTRUCTION AREAS.

For further information: Contact **Lucien Allen**, the **Community Construction Liaison** at (917) 270 - 2370 or **BrooklynCCL@bbjnyc.com**

Eric Adams,
Mayor

Thomas Foley, P.E.
Commissioner

Overview of Dismantle Activities & Progress


Interim sally port & officer booth

North Yard Demo & Berm Installation

275 Atlantic Ave.

Perimeter Wall Removal

MTA Vent Shafts

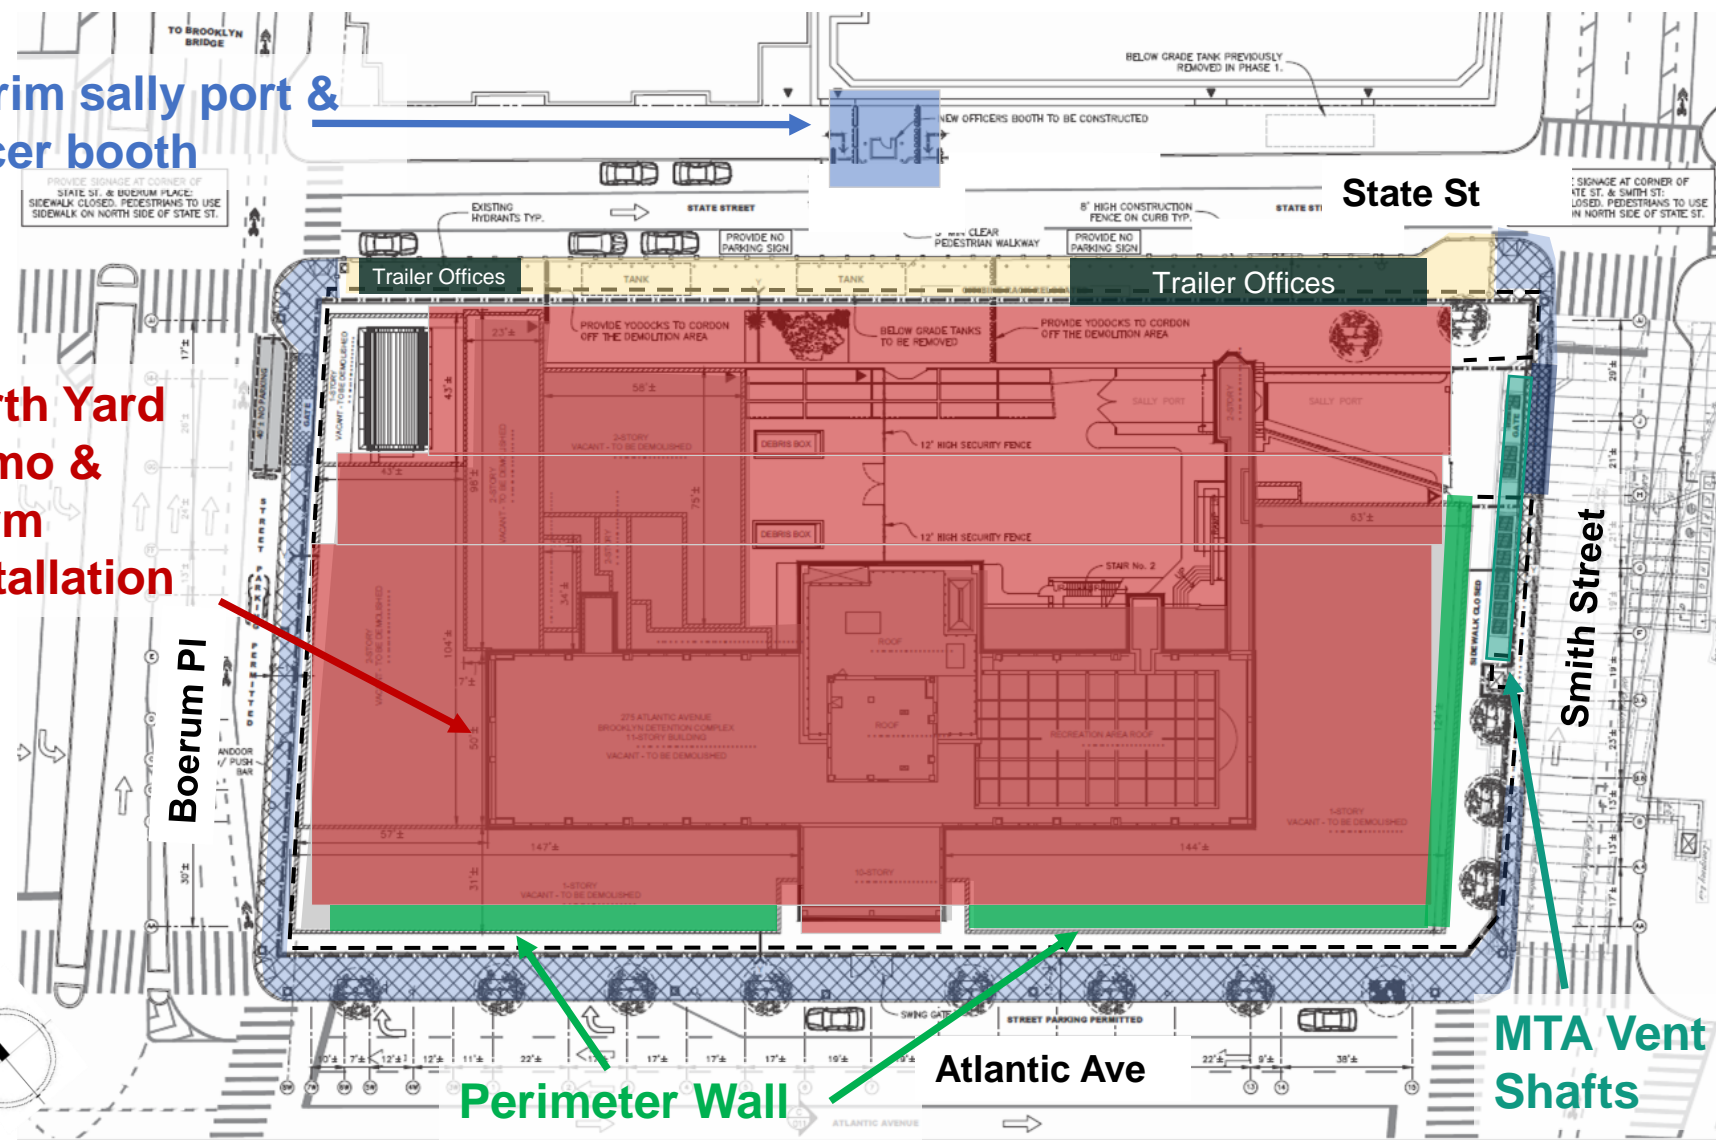

	8' HIGH SIDEWALK SHED
	16' HIGH SIDEWALK SHED
	CONSTRUCTION PLYWOOD FENCE
	SECURITY FENCE
	8' HIGH CONSTRUCTION FENCE ON CURB TYP.
	TA GRATING OVER VENTILATION STRUCTURE
	FIRE DEPARTMENT CONNECTION FOR SPRINKLER & STANDPIPE TO REMAIN
	DIRECTION OF TRAFFIC
	TREE WITH PROTECTION
	FIRE HYDRANT
	STREET SIGN
	YODOCKS TYP
	Sidewalk Closure
