

WEEKLY CONSTRUCTION BULLETIN

(5/31/25 – 6/8/25)

Brooklyn Facility Project PROJECT#: BBJ-KFAC BOROUGH: BROOKLYN DATE ISSUED: (5/30/25)

The following is an anticipated work schedule for the upcoming week. However, due to unforeseen field and weather conditions, it may become necessary to change some scheduled work locations, operations, and dates


DATE(S)	WORK HOURS	LOCATION	OPERATION
5/31/25 – 6/7/25	Tu – F / 7:00 am – 12:00 am Sat / 9:00 am – 5:00 pm	(275 Atlantic Avenue)	Foundation construction (Noise / Vibrations / Backfill site floor and pouring concrete for building foundation and slab / Work will take place inside the perimeter fencing)
5/31/25	Sat / 9:00 am – 5:00 pm	(275 Atlantic Avenue)	Test pit drilling (Noise / Vibrations / Drilling within site perimeter to probe for buried site utilities / A work zone will be temporarily created at Smith St. and Atlantic Ave. for one test pit outside of the site perimeter. / Vehicles access on Smith St. will remain. / Flaggers will direct pedestrians traffic as necessary.)
5/31/25 – 6/7/25	Tu – F / 7:00 am – 12:00 am Sat / 9:00 am – 5:00 pm	(275 Atlantic Avenue)	Boerum Pl. sidewalk reconstruction and shed construction (Noise / Vehicular and pedestrian access restrictions. / Construction of a sidewalk shed along Atlantic Ave. and Boerum Pl. / Atlantic Ave. pedestrian walkway will be open from 7 am - 10 am and 6 pm – 12 am; flaggers directing pedestrians as necessary. / From 10 am - 6 pm, pedestrians will be directed across the perimeter of the site on Atlantic Ave. to accommodate the TPC work zone for utility tie-ins.)
5/31/25 – 6/7/25	Tu – F / 10:00 am – 6:00 pm Sat / 9:00 am – 5:00 pm	(275 Atlantic Avenue)	Atlantic Ave. utility tie-ins (Noise / Vibrations / Saw-cutting the roadway and jackhammering to excavate road materials to expose existing utility connections and install new utility tie-ins / Flaggers will direct pedestrian traffic as necessary)
6/6/25 – 6/8/25	Fri - Sun / 9:00 pm (Friday) – 11:59 pm (Sunday)	(275 Atlantic Avenue)	Tower crane #2 delivery and installation (Noise / Vibrations / Vehicular and pedestrian access restrictions / Delivery of tower crane and installation on Boerum Pl. by use of a Mobile Hydraulic crane. / Pedestrian walkway will be closed and one north-bound lane will be occupied on Boerum Pl. / State St. access will be open to authorized vehicles <u>ONLY</u> via Smith St. / Pedestrian access to State St. will remain. Flaggers will direct truck and crane operations and pedestrians / Work will be conducted throughout the weekend.)

(NO PARKING SIGNS: WILL BE DISTRIBUTED/POSTED 72 HOURS PRIOR TO THE TEMPORARY ELIMINATION OF STREET PARKING. PLEASE OBSERVE POSTED PARKING REGULATIONS IN CONSTRUCTION AREAS.)

For further information: Contact **Lucien Allen**, the **Community Construction Liaison** at (917) 270 - 2370 or BrooklynCCL@bbjnyc.com

Eric Adams,
Mayor

Thomas Foley, P.E.
Commissioner

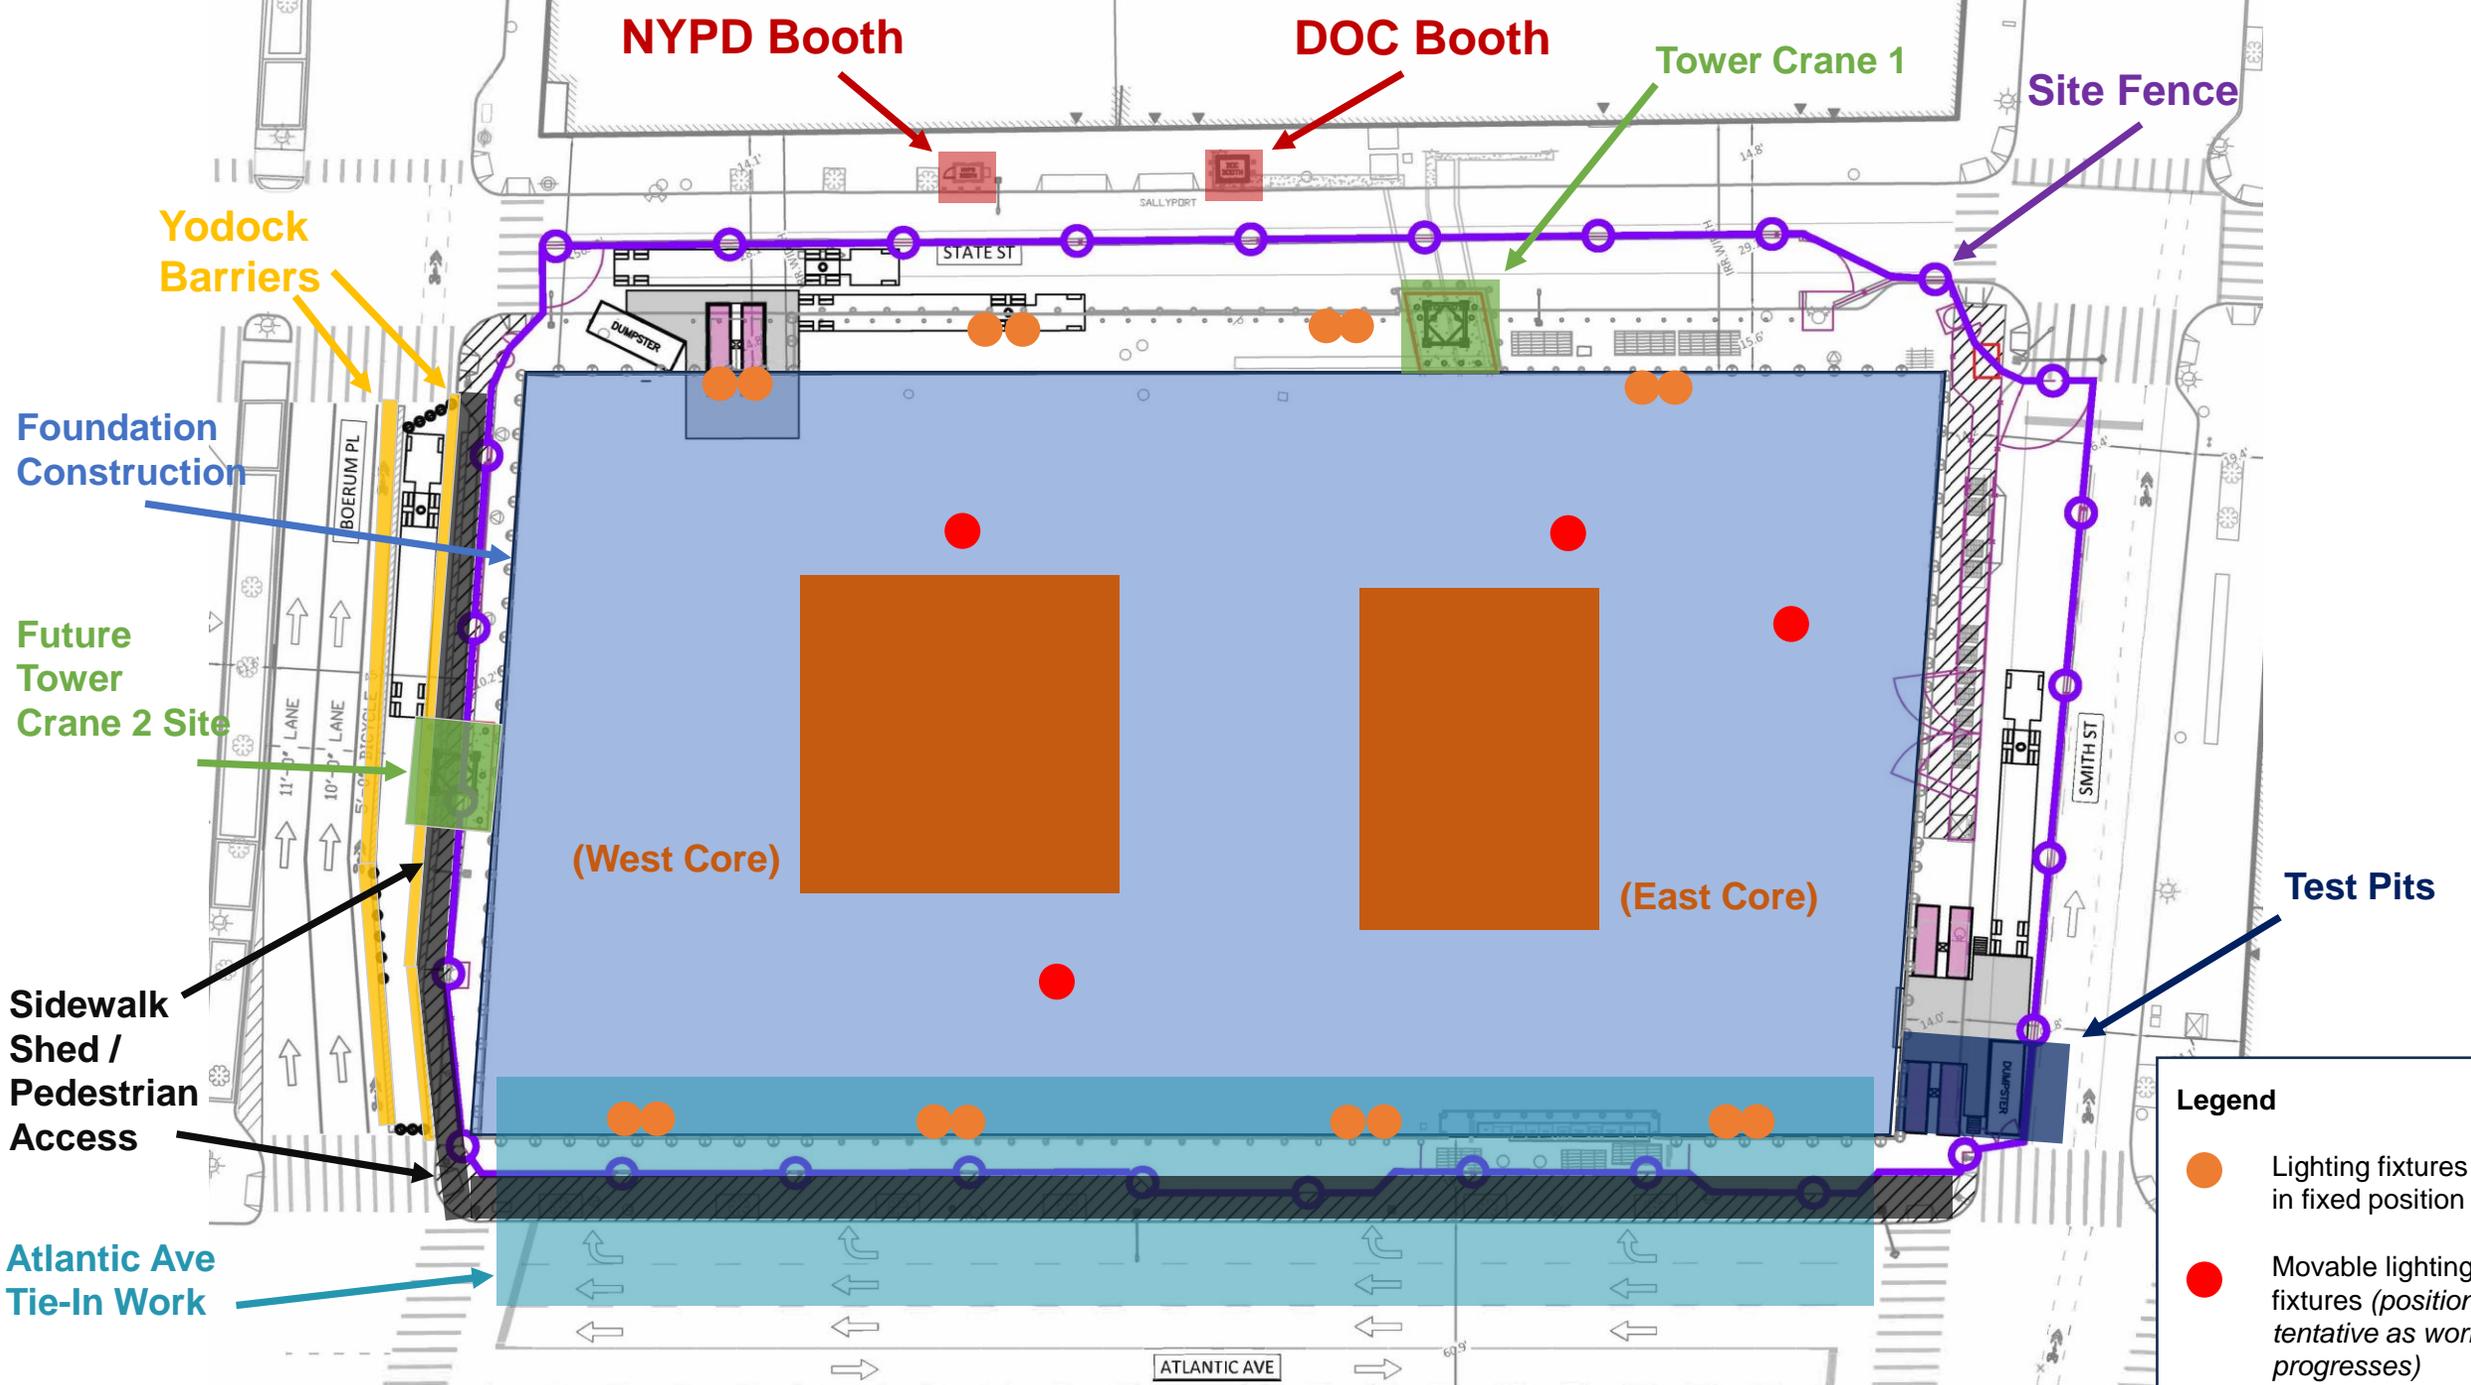

NYPD Booth

DOC Booth

Tower Crane 1

Site Fence

Yodock Barriers

Foundation Construction

Future Tower Crane 2 Site

(West Core)

(East Core)

Sidewalk Shed / Pedestrian Access

Atlantic Ave Tie-In Work

Test Pits

Legend

Orange circle: Lighting fixtures in fixed position

Red circle: Movable lighting fixtures (position tentative as work progresses)
